orm MI-ENG-100
Rev. 6/69

UNITED STATES DEPARTMENT OF AGRICULTURE
SOIL CONSERVATION SERVICE

TILE INSTALLATION DATA

Job Name Frank Zykowski

Section _____ Township _____ County Sag.

This report covers tile installation which was made according to current ACP specifications for tile drainage.

On jobs where there is a question of meeting specifications call the Soil Conservation Service Office before starting construction.

Return completed form to SCS office as soon as job is completed.

TILE INSTALLATION DATA

Mains and Single Lines						Outlet Pipe				
Main or Line	Tile Size	Drain Area	Drain Coeff.	Grade	Length	Kind	Size		Rodent Guard	Vert.* Clear.
							Diam.	Length		
	Inches	Acres	Inches	Ft/100	Feet	Mat'l.	Inches	Feet	No.	Feet
in A	6"	5	3/8	.1+	600	CMP	6"	14'	Yes	.1

Laterals

Total Length 4" 45.00 Ft.
Total Length 5" _____ Ft.
Min. grade 4" _____ Ft/100 Ft.
Min. grade 5" _____ Ft/100 Ft.
Min. Cover 2.4 Ft.

Type of blinding or filter used Backfiller & Plow
Area Tiled this year _____ Ac.
Tile spacing 60' Ft.
Type fittings used Main
Tile Manufactured by ADS

*Vertical Clearance - distance from low water in ditch to bottom of outlet pipe.

I certify that this report is correct. Tile were installed in the location shown on the sketch on reverse side. 4/18/77 Month Year


_____ Signature of owner or operator _____ Date

By William P. Pennington Signature of Contractor 4/18/77 Date
Halfhaus Trenching Services.

Form MI-ENG-100
Rev. 6/69

United States Department of Agriculture
Soil Conservation Service

TILE DRAINAGE PLAN

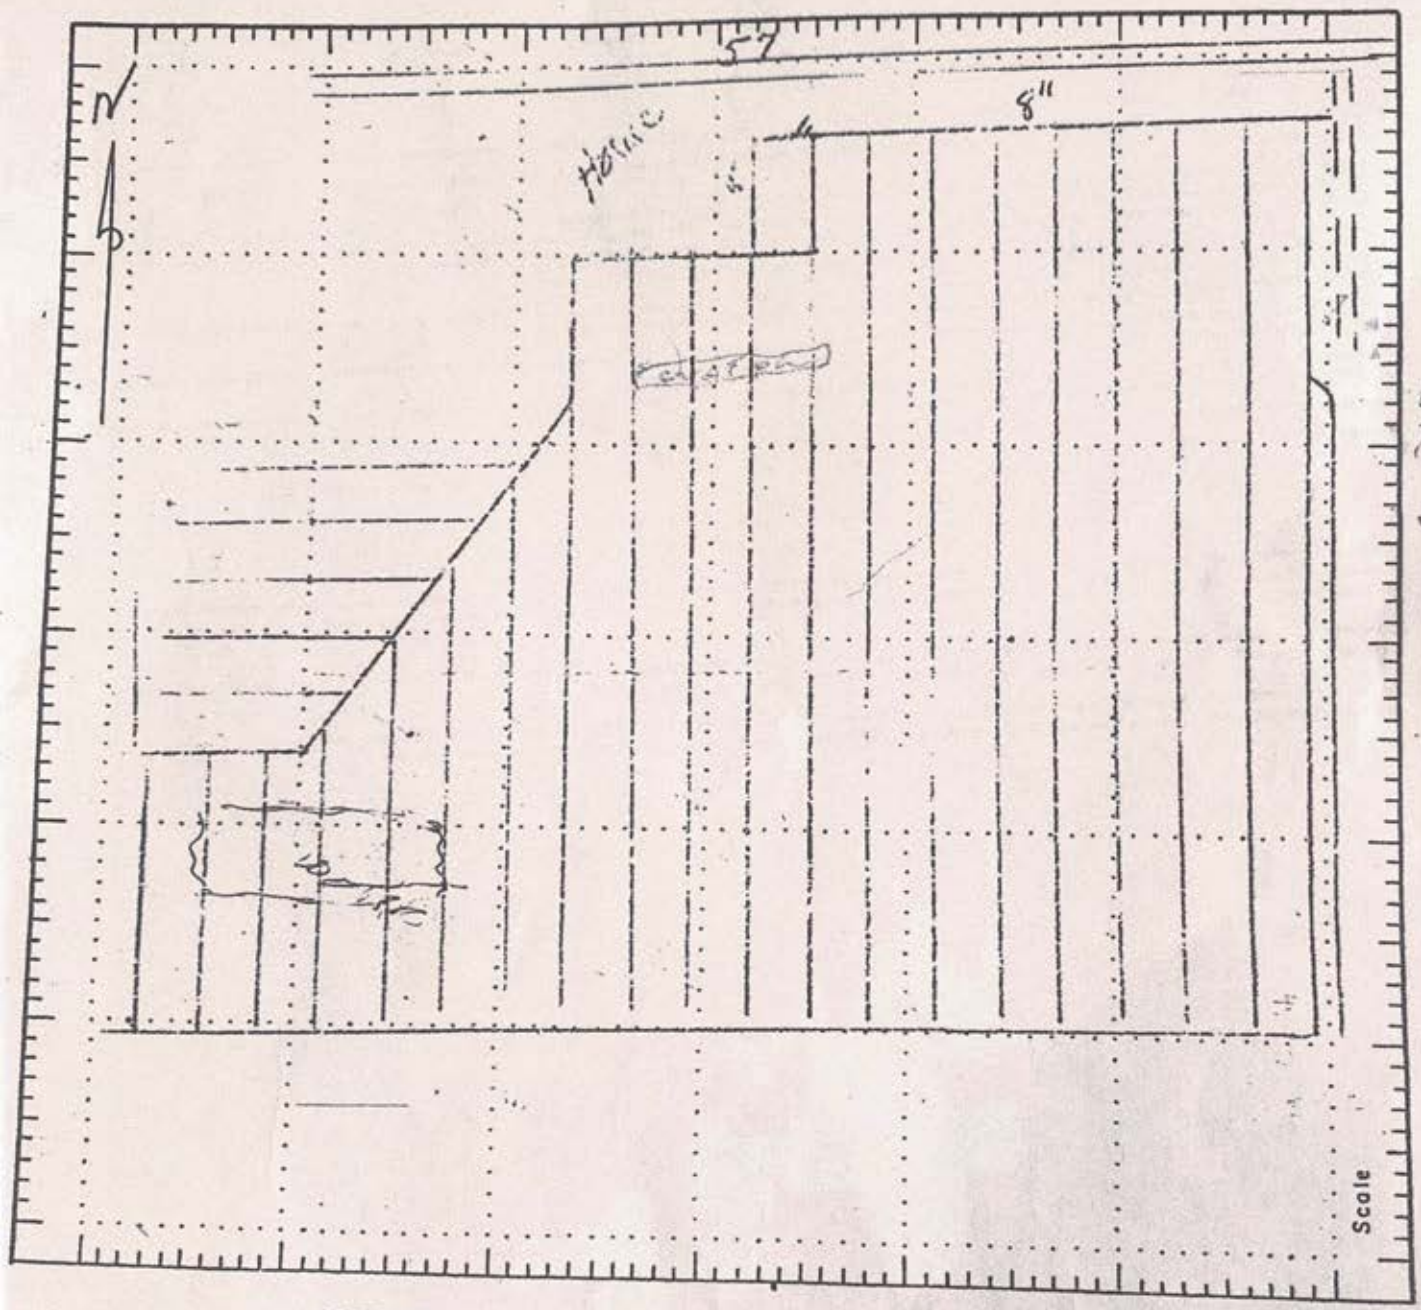

—LEGEND—

Road
Farm Boundary
Permanent Fence
Existing Tile Line
Proposed Tile Line
New Tile Installed
Existing Deep Ditch
Proposed Deep Ditch
Existing Shallow Ditch
Proposed Shallow Ditch


Remarks

SA-SCS-LINCOLN, NEBR. 1969

S.L-27,555

United States Department of Agriculture
Soil Conservation Service

TILE DRAINAGE PLAN

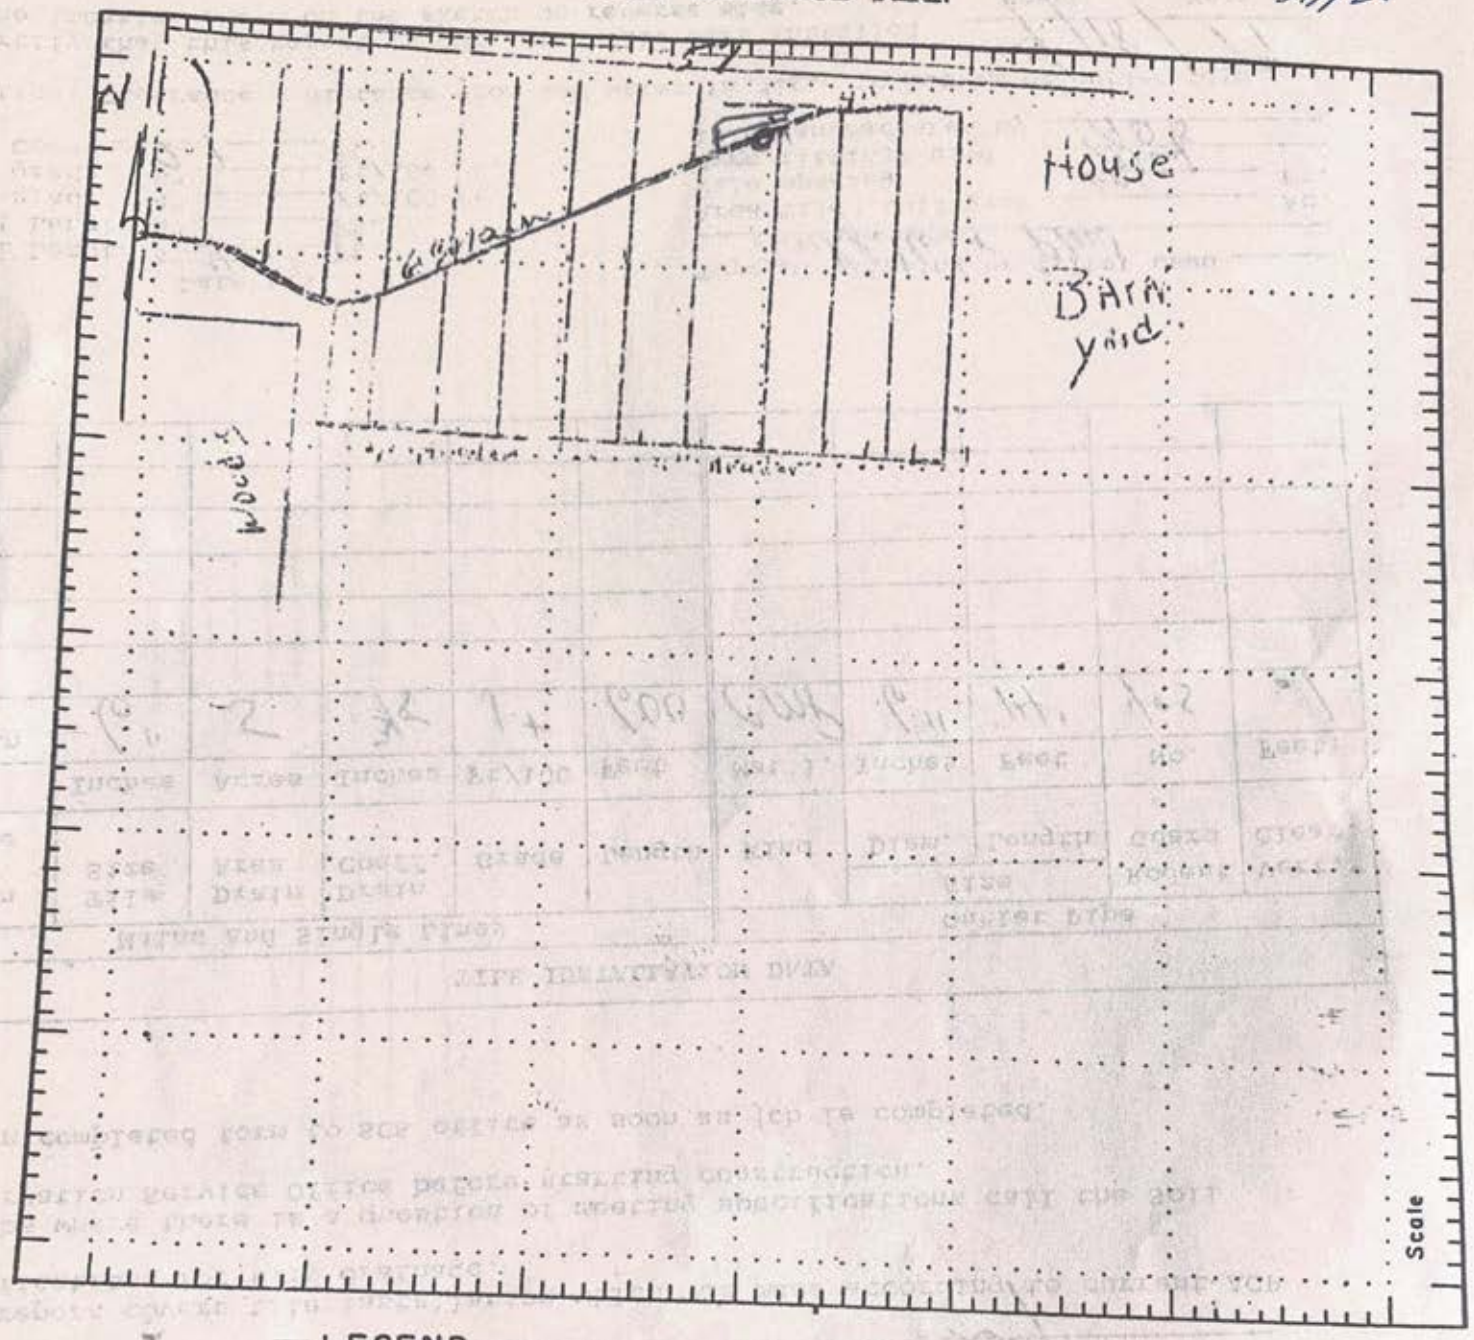

— LEGEND —

Road
Farm Boundary
Permanent Fence
Existing Tile Line
Proposed Tile Line
New Tile Installed
Existing Deep Ditch
Proposed Deep Ditch
Existing Shallow Ditch
Proposed Shallow Ditch


Remarks
5 Acre fill West of House and Barn yard.

USDA-SCS-LINCOLN, NEBR. 1969

S.L-27,555

Frank Lyrowski

M-57

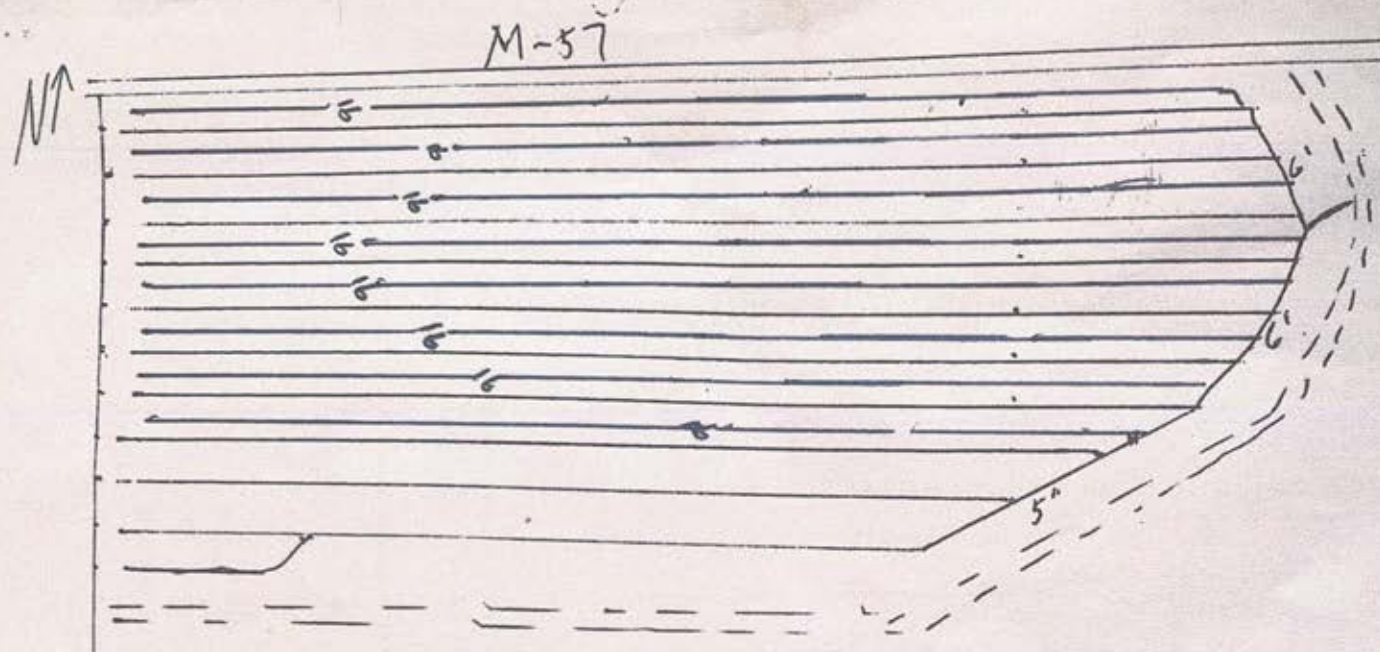

58' spacing

T.L.E. Split 1991

ENNINGTON FARM DRAINAGE
3885 W Sharon Road
AKLEY, MI 48649 US
989) 413-1940
fdrainage@gmail.com

Invoice



FRANK ZYROWSKI
300 BRADY ST
CHESANING, MI 48616

2104	06/18/2020	$14,929.00	06/18/2020	Net 30

4" tile	23,350	0.28	6,538.00
Fittings Taps tees outlets risers	25	20.00	500.00
6A STONE	4	35.00	140.00
		Subtotal:	7,178.00
Labor:TILING:4" installation	23,350	0.26	6,071.00
Labor:TILING:locating	14	120.00	1,680.00
	BALANCE DUE		$14,929.00

Paid in full
6-30-2020
MDD
thank you!
